

Finance and Administration Committee March 22, 2022

Information Item

FAC-6 UNCG Facilities Design and Construction Update

Background Information

Attachment (see below):

FAC-6.1 Facilities Design and Construction Project Update since 11.30.21
Board of Trustees Meeting with Photos of Projects Currently Under Construction

Robert J. Shea, Jr.

Bolort J. Sleaf.

Vice Chancellor for Finance and Administration

Facilities Design and Construction Project Update

Project ID	Building/ Location	Project	Funding Source	Project Development Phase	Bid Date	Construction Completion Date	Project Budget	Executive Status
2021-835	Alumni House	Interior Design Update	Other	Closed			N/A	Project Closed since last BOT mtg.
2021-837	Coleman	First Flr Lobby Elec. Outlet Installation	Dept. Funds	Closed	N/A	N/A	N/A	Project Closed since last BOT mtg.
2021-815	Coleman	Rooms 201 and 202 Dance Studio Curtain Installation	Dept. Funds	Closed	5/13/2021	12/13/2021	\$51,600	Project Closed since last BOT mtg.
2021-827	821 S Boyd St	Area 138 Hallway Door Installation	Dept. Funds	Closed	8/26/2021	10/13/2021	\$2,700	Project Closed since last BOT mtg.
2021-807	Moran Commons	Fountain View Alterations	Campus Enterprises	Closed	N/A	7/31/2021	\$500,000	Project Closed since last BOT mtg.
42025-321	Music Building	Exterior Walkway Repair and Waterproofing	R&R	Closed	4/22/2021	7/16/2021	\$230,375	Project Closed since last BOT mtg.
41525-302	Ragsdale Mendenhall Residence Hall	Roof Replacement	HRL Receipts	Closed	2/1/2019	6/30/2020	\$1,030,000	Project Closed since last BOT mtg.
N/A	South Josephine Boyd Street	Roadway and Sidewalk Improvement	POCAM	Closed	11/5/2021	8/6/2021	N/A	Project Closed since last BOT mtg.
2021-786	Sullivan	Room 221 Alterations	Dept. Funds	Closed	5/4/2021	8/23/2021	\$117,263	Project Closed since last BOT mtg.
2021-831	UNCG Auditorium	Chandelier Suspension Mechanism Upgrade	Dept. Funds	Closed	8/2/2021	1/7/2022	\$33,600	Project Closed since last BOT mtg.
TOTAL PRO	DJECTS CLOSED:	 = 10					TOTAL F	BUDGET: \$1,965,538

Repair Completed Complete	Project ID	Building/ Location	Project	Funding Source	Project Development Phase	Bid Date	Construction Completion Date	Project Budget	Executive Status
Alumni House Blackboard Installation House Rental Income Completed 2/12/2021 7/20/2021 582,800 Project in Close-out.	2021-796	326 Tate Street	Envelope	Dept. Funds	Completed	8/24/2021	12/7/2021	\$77,000	Project in Close-out.
2021-825 Coleman Carpet Replacement Replac	2019-707	Alumni House		House Rental	Completed	2/12/2021	7/20/2021	\$82,800	Project in Close-out.
Alterations Dept. Funds Completed 6/22/2021 11/30/2021 S132,300 Project in Close-out. Moran Commons Project Administration Completed N/A N/A N/A N/A N/A N/A Project in Close-out. Horizon AVL requested card access to rekey ITS/Mechanical rm. 2021-808 Moran Commons Spartan Market Upfit Commons Spartan Market Upfit Enterprises Completed N/A 7/30/2021 \$300,000 Project in Close-out. 1625-304A Walker Parking Deck Girder Repairs POCAM Completed 2/16/2021 8/13/2021 \$300,000 Project in Close-out. Classroom Technology Upgrade Dept. Funds Way 2022 Funds On Hold until May 2022 Project in Close-out. NIB and SCP New Construction NC Bond Close-out A/26/2018 10/30/2020 \$105,000,000 Project in Close-out odderess a new list of add'l work items that will be handled outside of the CM@R contract and w/ minimal involvement from design team.	2021-825	Coleman	Carpet	Dept Funds	Completed	8/22/2021	11/5/221	\$28,200	Project in Close-out.
Moran Commons Moran Commons Moran Commons Moran Commons Moran Commons Spartan Market Campus Enterprises Completed N/A N/A N/A N/A N/A N/A Horizon AVL requested card access to rekey ITS/Mechanical rm. Commons Spartan Market Campus Enterprises Completed N/A 7/30/2021 \$300,000 Project in Close-out. Completed N/A N/A N/A N/A N/A N/A N/A N/	2021-789	Forney		Dept. Funds	Completed	6/22/2021	11/30/2021	\$132,300	Project in Close-out.
Commons Upfit Enterprises Completed N/A 7/30/2021 \$300,000 Project in Close-out. Walker Parking Deck Girder Repairs POCAM Completed 2/16/2021 8/13/2021 \$300,000 Project in Close-out. 2021-814 Music Building Classroom Technology Upgrade Dept. Funds May 2022 Popt. Funds May 2022 Popt. Funds Project in Close-out. NIB and SCP New Construction NC Bond Close-out NC Bond NC B	2021-803		Project		Completed	N/A	N/A	N/A	Horizon AVL requested card access to rekey
Deck Girder Repairs POCAM Completed 2/16/2021 8/13/2021 \$300,000 Project in Close-out. Classroom Technology Upgrade Dept. Funds On Hold until May 2022 6/10/2021 10/25/2021 \$112,200 Installation takes 2 wks to complete. Dept. reserved rooms starting 5/16/22. NIB and SCP New Construction NC Bond Close-out NC Bond Close-out A/26/2018 10/30/2020 \$105,000,000 Warranty items is ongoing. Starting to address a new list of add'l work items that will be handled outside of the CM@R contract and w/ minimal involvement from design team.	2021-808				Completed	N/A	7/30/2021	\$300,000	Project in Close-out.
2021-814 Music Building Technology Upgrade Dept. Funds On Hold until May 2022 6/10/2021 10/25/2021 \$112,200 to complete. Dept. reserved rooms starting 5/16/22. NIB and SCP New Construction NC Bond Close-out NC Bond NC Bon	41625-304A	-	Girder Repairs	POCAM	Completed	2/16/2021	8/13/2021	\$300,000	Project in Close-out.
NIB and SCP New Construction NC Bond Close-out A/26/2018 10/30/2020 \$105,000,000 Warranty items is ongoing. Starting to address a new list of add'l work items that will be handled outside of the CM@R contract and w/ minimal involvement from design team.	2021-814	Music Building	Technology	Dept. Funds		6/10/2021	10/25/2021	\$112,200	to complete. Dept. reserved rooms starting
	46625-301	NIB and SCP			Close-out	4/26/2018	10/30/2020	\$105,000,000	Warranty items is ongoing. Starting to address a new list of add'l work items that will be handled outside of the CM@R contract and w/ minimal involvement from design
OTAL PROJECTS COMPLETED = 9 TOTAL BUDGET: \$106,032,500	TOTAL PRO	FCTS COMPLET	FD = 9					TOTAL	 BUDGET: \$106,032,500

Project ID	Building/ Location	Project	Funding Source	Project Development Phase	Bid Date	Construction Completion Date	Project Budget	Executive Status	
2021-851	Alumni House	100F Hallway Door Installation	Dept. Funds	Construction	2/3/2022	4/15/2022	\$6,400	Contractor keeping FDC informed on status of long lead items.	
2021-820	Coleman	Room 338 Renovation	Dept. Funds	Construction	12/7/2021	4/18/2022	\$124,300	Construction is underway and on schedule.	
42025-321	Gatewood Studio Arts / Roof	Replace Skylight. Repair Roof Deck.	R&R	Construction	4/15/2021	7/15/2022	\$205,300	Awaiting REI's notes on change order requested.	
2021-806	Moran Commons	Taco Bell Renovation	Campus Enterprises	Construction	N/A	2/15/2022	\$1,050,000	General contractor report, testing has gone well.	
2021-840	Moran Commons	Access Control	Campus Enterprises	Construction	2/15/2022		\$71,500	Pre-con mtg was held on 3/8.	
2021-813	Music Building	Interior Blackboard Access Installation	Dept. Funds	Construction	9/28/2021	9/30/2022	\$64,400	Request from Fac/Ops asking to consider adding exterior doors to the project to cmply w/ Transact Master Plan.	
42025-331	Music Building	Roof Replacement (Recoating)	R&R	Construction	12/2/2021	8/7/2022	\$791,063	Triad Roofing contract sent to F&A for signatures.	
2021-830	UNCG Auditorium	Audio Upgrades	Dept. Funds	Construction	9/1/2021	1/7/2022	\$179,000	Awaiting the vendor to complete the punch list items. Coordination with auditorium staff and availability.	
2020-780	Walker Parking Deck	Elevator Modernization	Campus Enterprises	Construction	4/5/2021	3/8/2022	\$324,500	Working on activating ports for phone and video systems. Awaiting to schedule DOL inspection.	
	IFOTO IN CONTR	EDITORIO : C							
TOTAL PROJECTS IN CONSTRUCTION= 9 TOTAL BUDGET= \$2,816,463									

Project ID	Building/ Location	Project	Funding Source	Project Development Phase	Bid Date	Construction Completion Date	Project Budget	Executive Status
2022-865	1100 W Market Street	UTLC Suite Modifications		Design				Drafting POR. Mtg was held on 3/9 to discuss office move and third floor scope.
2022-863	Brown	Laundry and Wardrobe Room 039	Dept Funds	Design				Held a follow up scoping mtg w/ end users on 3/7.
2021-799	Bryan	416 Renovation		Design			\$55,800	Contract fully signed and submitted to the AE on 3/4.
2021-824	Campus- General	Parking Deck Assessments	POCAM	Design			\$86,400	Reports were received, and are under review. Awaiting comments.
	Campus- General	Chilled Water Infrastructure & Equipment Improvements	R&R	Design	1/17/2023		\$10,400,000	Designer interviews were held March 9th. Designer recommendation was provided to the BOT.
41725-301	Campus- General	Steam Distribution System Replacement PH IVB	R&R	Design	7/29/2022		\$1,720,000	Awaiting funding confirmation to be able to proceed.
2021-828	Campus- General	Underground Heating Hot Water Piping Replacement	R&R	Design	3/24/2022	7/15/2022	\$256,200	Alternate piping materials suggested during Pre-bid are under review.
2021-817	Campus- General	Microbobility/Cyclist Signage and Striping Phase 1	POCAM	Design			\$20,000	Virtual mtg of the review group is scheduled for 3/28.
2022-859	Campus Supply	Fuel Pump Upgrades		Design				Purchase of a design/build system is being investigated.
2022-869	Coleman	420J Alterations Budget		Design				Project manager assigned to project.
2019-682	Coleman	Room 332 Coaches Suite Alterations	Capital	Design	3/15/2022	8/15/2022	\$476,000	Bid opening was held 3/15.
2022-866	Coleman	Office to Student Lounge Conversion- Room 339	Dept Funds	Design				Scope mtg was held 3/2. POR was submitted to customer on 3/11.
2021-842	Coleman	Men's Basketball Team Lounge- Part 2	Dept. Funds	Design	1/27/2022		\$10,500	Contract is executed. Purchase order sent to contractor.
41725-323	Coleman	Fire Alarm System Replacement	R&R	Design	7/22/2022		\$2,491,608	Held meeting w/ designer to discuss proposal for the budget and schedule.
2021-847	Cone Art	Lighting and Controls Replacement Phase 2&3	R&R	Design	9/20/2023		\$961,800	Designer advertisement being finalized to post.
2021-802	Foust	Fac Condition Assessment		Design	N/A	N/A	N/A	Architect site visit occurred on 3/3/22. Expecting draft FCA.
	Jackson Library	Addition & Renovation	Other	Design	4/5/2024	5/3/2027	\$81,000,000	Designer interviews were held 3/16. Designer recommendation was submitted to BOT. Preparing the CM@R advertisement.
2021-837	Lexington Residence Hall	205R HVAC Solution	Dept. Funds	Design			\$17,300	AEI's response to SCO sent for final review and approval.
2021-846	McCormick Residence Hall	Suite 101- Bestway Condensation Repair		Design				Designer proposal expected to be rec'd March 17.
2021-826	McCormick Residence Hall	Bestway Bulk Refrigeration		Design			\$20,000	Designer proposal expected to be rec'd March 17.

Moran Commons Arena Admin Office Campus Enterprises Design 7/14/2022 1/26/2023 \$82,500 AE(#2) visited site on 2/25, anticipate proposity 3/11, AE(#1) provided no response to requests.	Project ID	Building/ Location	Project	Funding Source	Project Development Phase	Bid Date	Construction Completion Date	Project Budget	Executive Status
2022-861 McNutt Minor Renovations Dept Funds Design SD/Do documents being compiled for design review exemption. Antenna Internal Internal Project manager assigned to project. Design 7/19/2022 12/1/2022 \$29,400 Designer is working on the deficiency report. Report expected by 3/16 Project manager assigned to project. Design 7/19/2022 12/1/2022 \$29,400 Designer is working on the deficiency report. Report expected by 3/16 Project manager assigned to project. Design 7/19/2022 12/1/2022 \$29,400 Designer is working on the deficiency report. Report expected by 3/16 Project manager assigned to project. Design 7/19/2022 1/26/2023 \$82,500 Designer is working on the deficiency report. Report expected by 3/16 Project is fully funded. Assembling the construction contract. Assembling the construction contract. Awaiting Affidiavit C from contractor. Design 2/22/2022 \$1/26/2023 \$82,500 Design 1/26/2023 \$82,500 Design 1/26/2023 \$82,500 Designer is working on the deficiency report. Report expected by 3/16 Project is fully funded. Assembling the construction contract. Awaiting Project is fully funded. Assembling the construction contract. Awaiting Duke Energy to green light the next phase. Program (Glemwood) Awaiting Duke Energy to green light the next phase. Program (Glemwood) Program (Glemwood	42125-302			POCAM	Design	9/22/2022		\$611,899	
2021-850 Moran Commons NW Exterior Campus Enterprises Design 7/19/2022 12/1/2022 \$29,400 Besigner is working on the deficiency report. Report expected by 3/16 Moran Commons Amelia Repair Enterprises Design 7/14/2022 12/1/2022 \$29,400 Besigner is working on the deficiency report. Report expected by 3/16 AE/R2) visited site on AE/R2) visited si	2022861	McNutt	Minor	Dept Funds	Design				SD/DD documents being compiled for design
2021-850 Moran Commons NW Exterior Wall Repair Enterprises Design 7/19/2022 12/1/2022 \$29,400 Enterprise Senterprises Design 7/19/2022 12/1/2022 \$29,400 Enterprise Senterprises Design 7/19/2022 1/26/2023 \$82,500 Senterprises Senterprises Design 7/14/2022 1/26/2023 \$82,500 Senterprises Senterprises Senterprises Design 7/14/2022 1/26/2023 \$82,500 Senterprises Senterprise	2022-867	McNutt							= =
2021-853 Moran Commons Arena Admin Office	2021-850			•	Design	7/19/2022	12/1/2022	\$29,400	Designer is working on
Music Building Recording Studio Dept Funds Design 2/22/2022 \$187,100 Assembling the construction contract.	2021-853		Arena Admin		Design	7/14/2022	1/26/2023	\$82,500	AE(#2) visited site on 2/25. anticipate proposal by 3/11. AE(#1) provided no response to requests.
Plug Program (Glenwood Ave) Piney Lake Create Master Plan	2018-628		Recording	Dept Funds	Design	2/22/2022		\$187,100	Assembling the construction contract. Awaiting Affidavit C from
2021-793 Piney Lake Create Master Plan N/A Design N/A N/A N/A Submitted to customer of 3/8. 42025-321 Stone Roof Replacement R&R Design 2/17/2022 7/29/2022 \$775,552 Awaiting funding confirmation. 2021-797 Stone College Tribute Sculpture Sculpture New Renovation Plan N/A Design N/A N/A N/A N/A Submitted to customer of 3/8. Design 2/17/2022 7/29/2022 \$775,552 Awaiting funding confirmation. CD documents are nearly complete and ready to be sent for University review. A noise monitor set up of site for acoustical measurements. SD progress mtg scheduled for 3/30. Taylor Theatre Renovation Plan Structure Reno	2021-855	Plug Program (Glenwood	•		Design				green light the next
Replacement R&R Design 2/17/2022 7/29/2022 5/75,552 confirmation. 2021-797 Stone College Tribute Sculpture Sculpture New Renovation Tate + Gate Replacement New Renovation Taylor Theatre Renovation Taylor Theatre Renovation Taylor Theatre Renovation Replacement R&R Design 2/17/2022 7/29/2022 5/75,552 confirmation. Design 3/29/2022 5/75,552 confirmation. Design 3/29/2022 5/75,552 confirmation. CD documents are nearly complete and ready to b sent for University review. A noise monitor set up o site for acoustical measurements. SD progress mtg scheduled for 3/30. Mtg held 3/7 finalize priority list w/ the Theatre Dept. Proposal kickoff mtg for CX services held 3/10.	2021-793	Piney Lake		N/A	Design	N/A	N/A	N/A	submitted to customer on
Stone College Tribute Sculpture Posign Jay 2022 Stone Sent for University Advancement Sculpture Tate + Gate Renovation Taylor Theatre Dept. Proposal kickoff mtg for CX services held 3/10.	42025-321	Stone		R&R	Design	2/17/2022	7/29/2022	\$775,552	
42025-302 Tate + Gate Renovation Punds Design 9/20/2022 6/3/2024 \$10,330,300 measurements. SD progress mtg scheduled for 3/30. Taylor Theatre Renovation Carry Forward Renovation Design 3/10/2023 \$10,504,664 Theatre Dept. Proposal kickoff mtg for CX services held 3/10.	2021-797	Stone	College Tribute	by University	Design	3/29/2022		\$216,400	·
42025-301 Taylor Theatre Renovation Building Infrastructure Renovation Design 3/10/2023 \$10,504,664 Theatre Dept. Proposal kickoff mtg for CX services held 3/10.	42025-302	Tate + Gate			Design	9/20/2022	6/3/2024	\$10,330,300	measurements. SD progress mtg scheduled
TOTAL PROJECTS IN DESIGN - 22	42025-301		Infrastructure	Carry Forward	Design	3/10/2023		\$10,504,664	priority list w/ the Theatre Dept. Proposal kickoff mtg for CX
	TOTAL PROI	ECTS IN DESI	 GN = 32					ΤΩΤΔ	 L BUDGET: \$120,253,423

UNCG Auditorium Audio Upgrades



New white speakers installed in the same location as the previous speakers.





Before



Installation of a new sound system that included speakers and subwoofers located behind the lattice work within the Organ Lofts, otherwise known as the Boom Area, on each side of the stage.

Gatewood Studio Arts Skylight Roof Deck Repair




After




Before

Esports Venue Project Administration Moran Commons Room 109

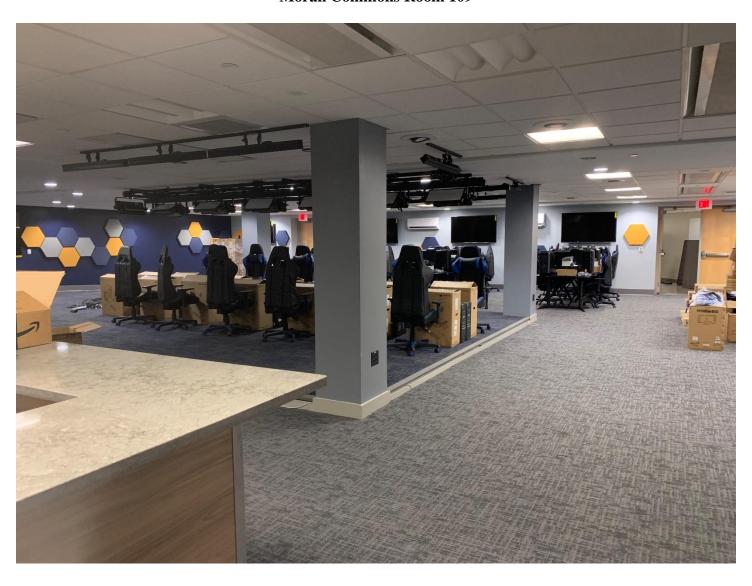

Walker Parking Deck Elevator Modernization

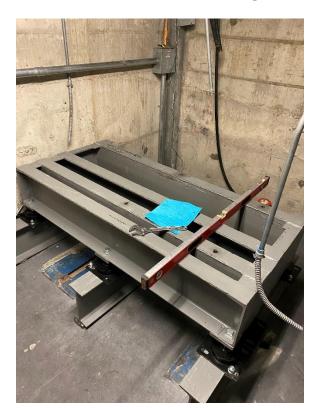



Forney 201 Alterations



